
14Ultimate.com

Your source for improvements to I-4 in Orange and Seminole counties



I-4 UIJIIMMAHH

IMPROVEMENT PROJECT

TINATE PROJECT UPORTS

City of Orlando Council Meeting ORCANDO





Project Overview

EMPROVEMENT PROJECT

21 miles from west of Kirkman Road to east of SR 434 Orange & Seminole Counties

Scope:

Reconstruct mainline and interchanges
Addition of 4 Express Lanes
Reconstructs 15 major interchanges
Bridges: widens 13; adds 53; replaces 74
Increases design speed to 60 mph

Operations and Maintenance

P3 - 40 year contract

Design-Build-Finance-Operate-Maintain

2,310 days (6.33 years) for design and construction

I-4 Mobility Partners


Concessionaire: Skanska, John Laing

Construction JV: SGL - Skanska Granite Lane

Design JV: Jacobs - HDR


Quality Assurance Firm (QAF): Volkert

\$2.323 billion (yoe) Design-Build cost

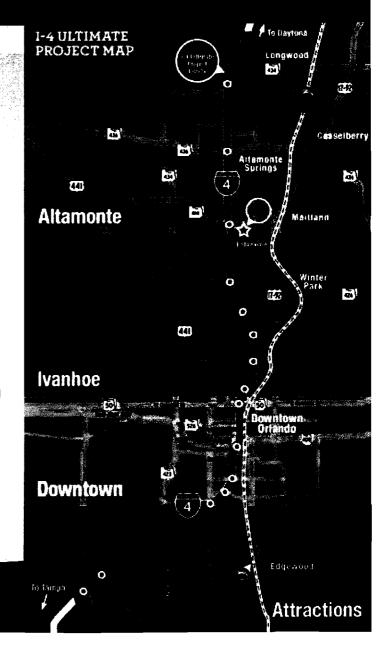



nterstate Typical Section

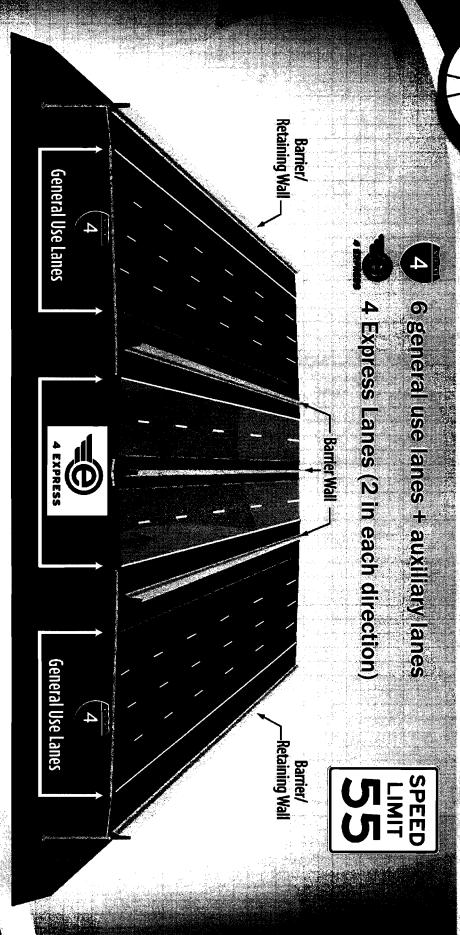



Planned Access to Express Lanes

OT sets toll rates and collects tolls

mited access to & from tolled express lanes

Barrier wall separated
Slip ramp access
Direct ramp access



Six to seven access points in each direction


Dynamic tolling

All Electronic Tolling

Everyone pays


No heavy trucks



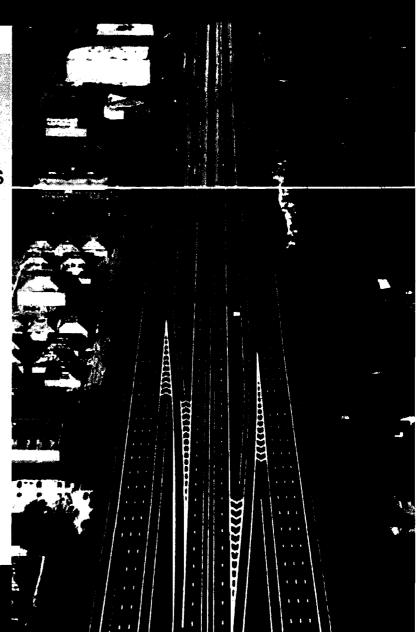



Aesthetics

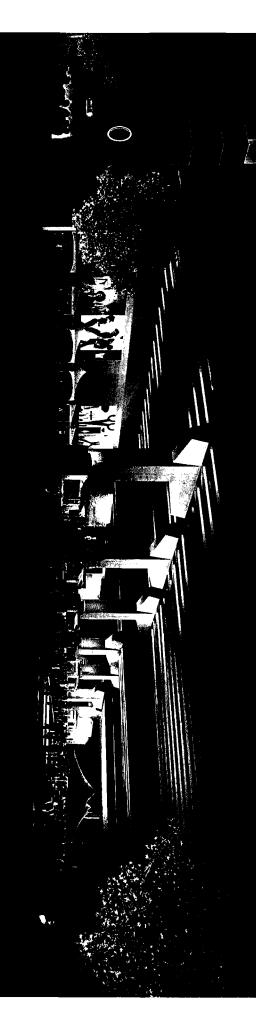



Aesthetics

I4Ultimate.com




-4 Ultimate - The first year +

October 2014 Eebruary 2015 Early 2021


Design began (NTP:1)


Construction and Operations and Maintenance began (NTP 2) Substantial/Final Completion of Design and Construction







O&M - The First Year

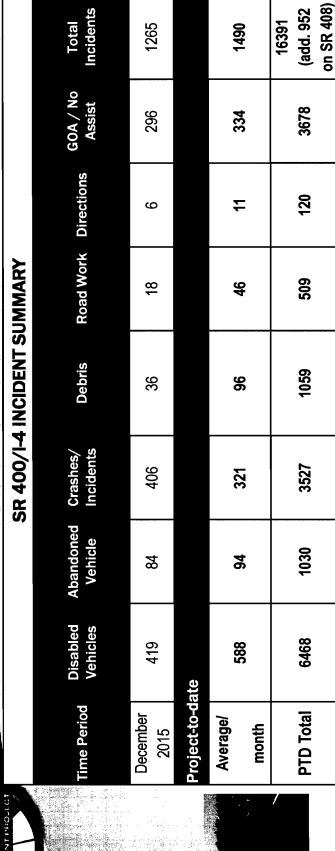











14Ultimate.com

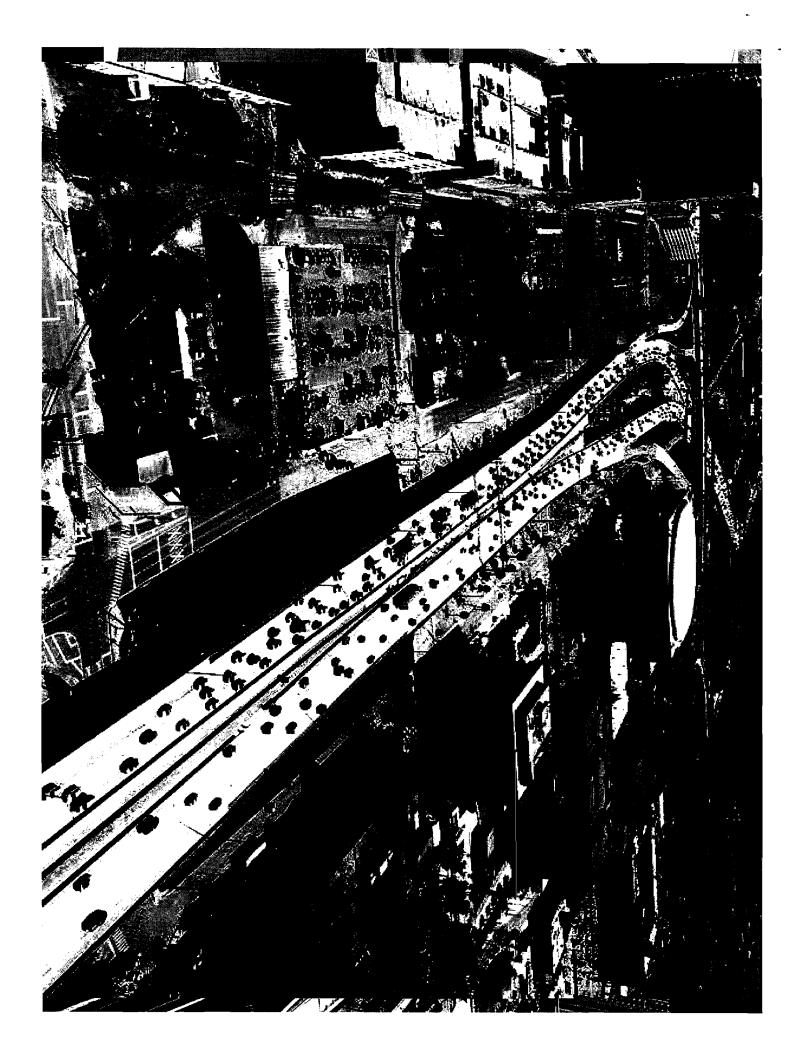

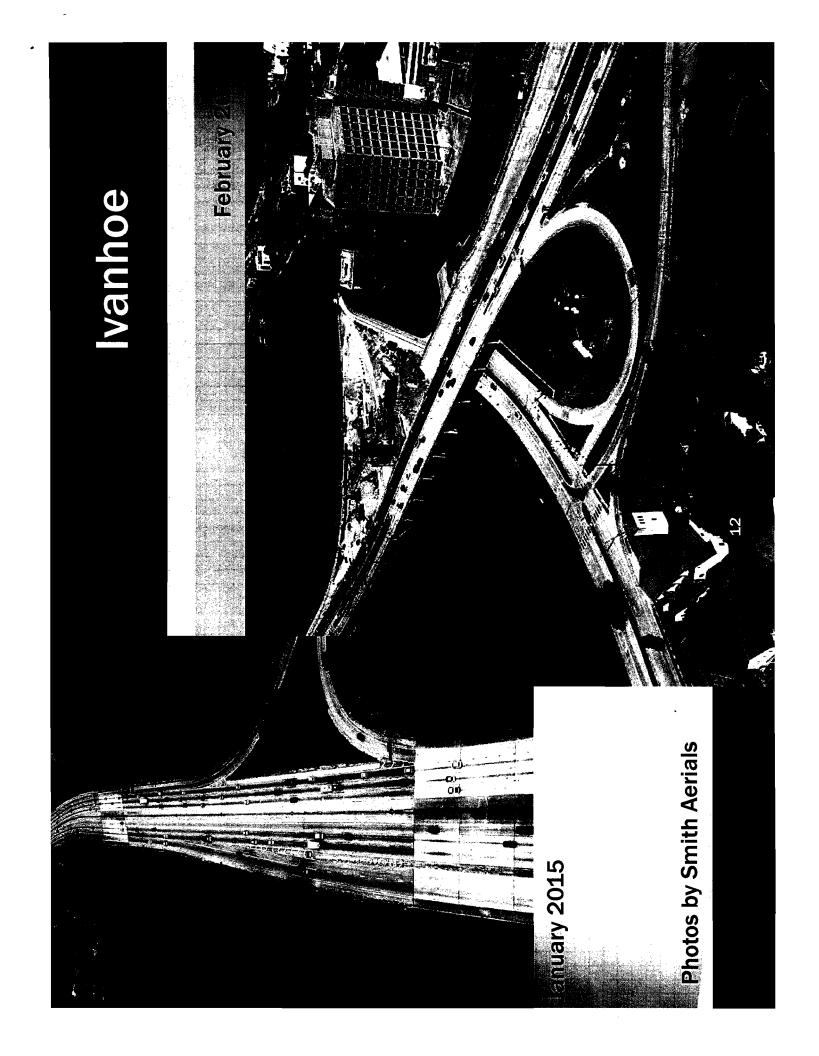

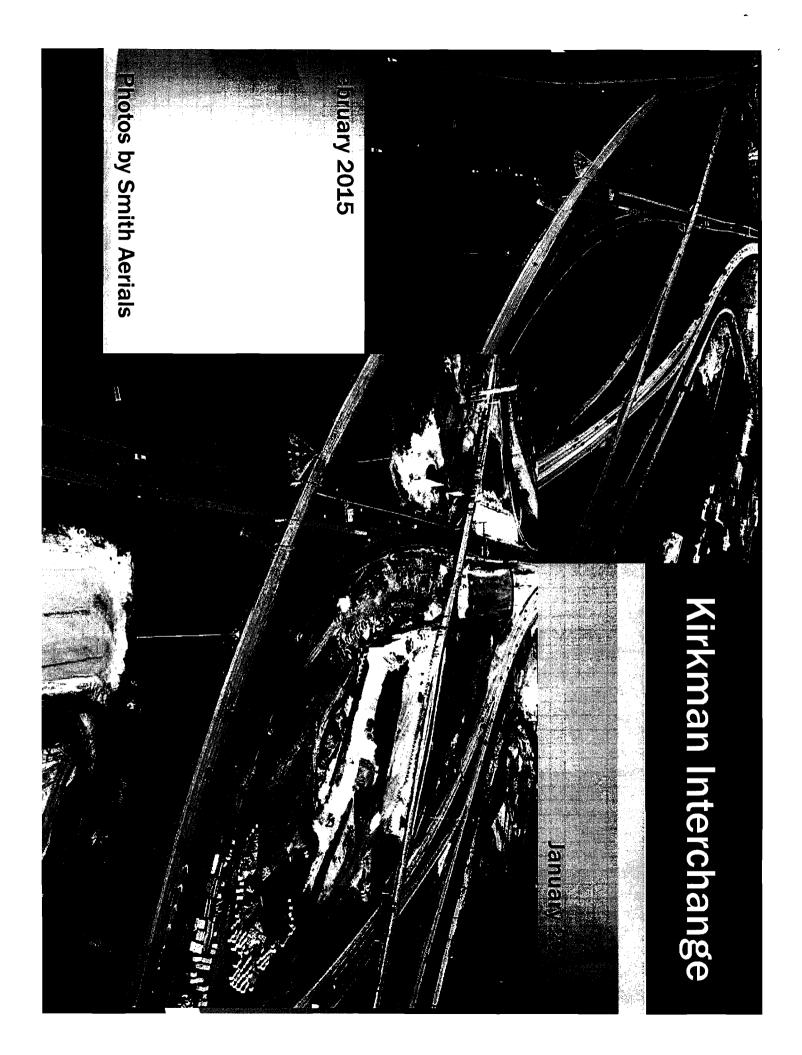



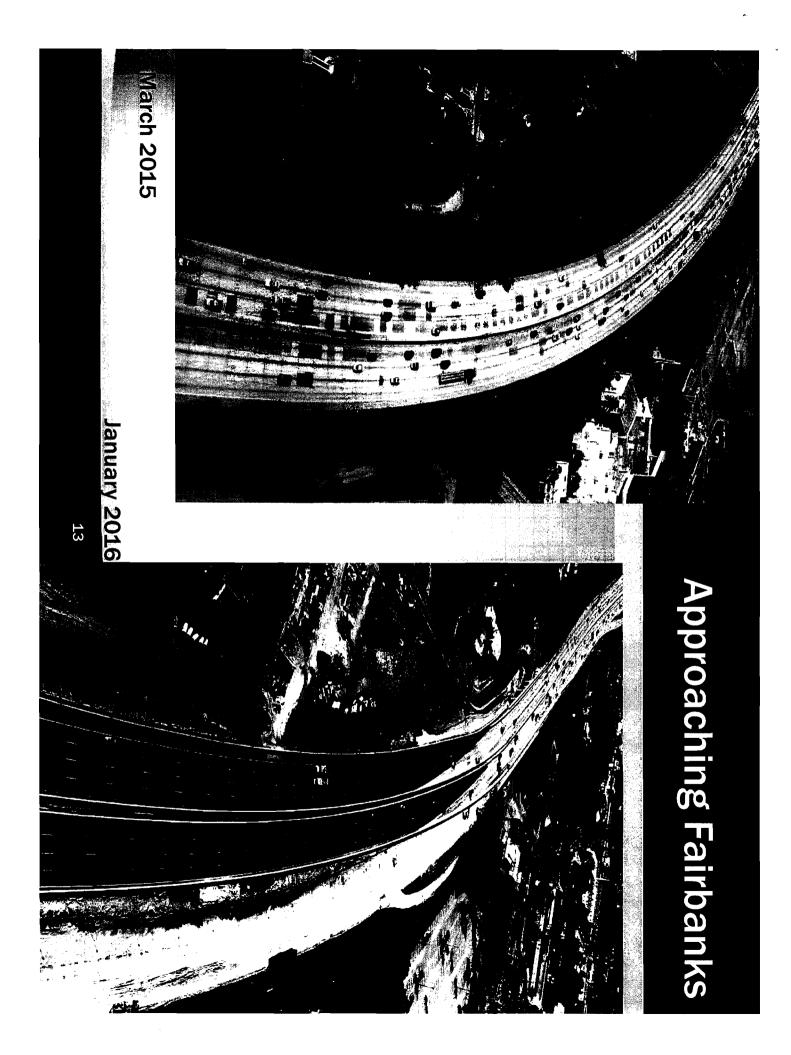




Sound Walls

Ground Mounted Sound Wall Installation

- estimated installation complete by end of March/early April 2016.
- West side of I-4: Gore St. to Raleigh St. (~1,000 ft)
- East side of I-4: Princeton St. to Yale St. (~500 ft)

Majority of the walls on the corridor will be shoulder mounted, which will be installed as the widening work occurs.

Locations and more about sounds walls, http://i4ultimate.com/projectinfo/special-features/, click on 'Sound Abatement' tab.






Recruitment, Training and Development Office - Downtown Orlando



Details on address, how to apply, etc can be found in

http://i4ultimate.com/project-info/working-on-i-4



ontact Information

844-750-4984

409 W Robinson, Orlando, FL

- 0.3 miles away from LYNX bus station
- Apply in person details on the website.

WorkForceDevelopment@SGLConstructors.com





General Project Schedule

Activity F 1	Start Start	Einish
Oncession Agreement Execution		9/4/2014
NTP 1 – Design	10/4/2014	-
NTP 2 – Construction and Operations & Maintenance	2/1/2015	_
Pile driving, lane shifts, drainage, utility relocations, econstruction ONGOING		<u>-</u>
Grand National Overpass – Open to traffic to be able to cross between the East and West sides of I-4		By Fall 2017
Substantial Completion	 -	January 2021
inal Acceptance	-	March 2021



Grand National

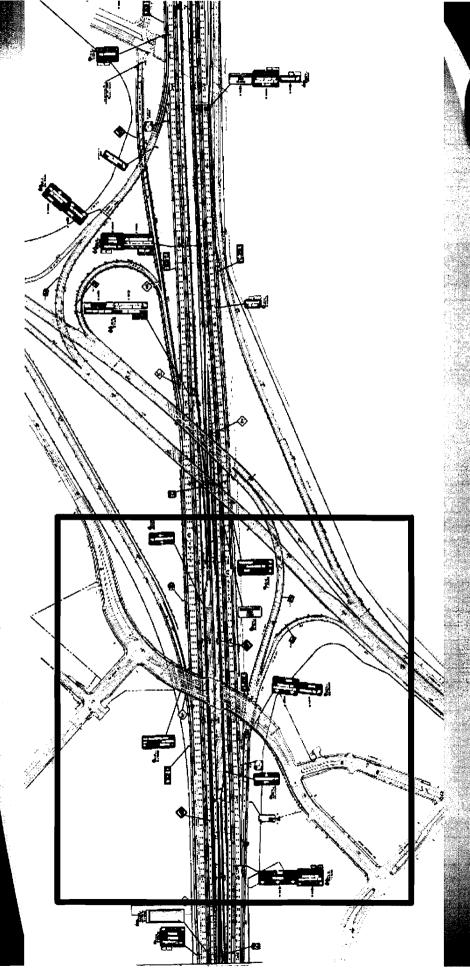

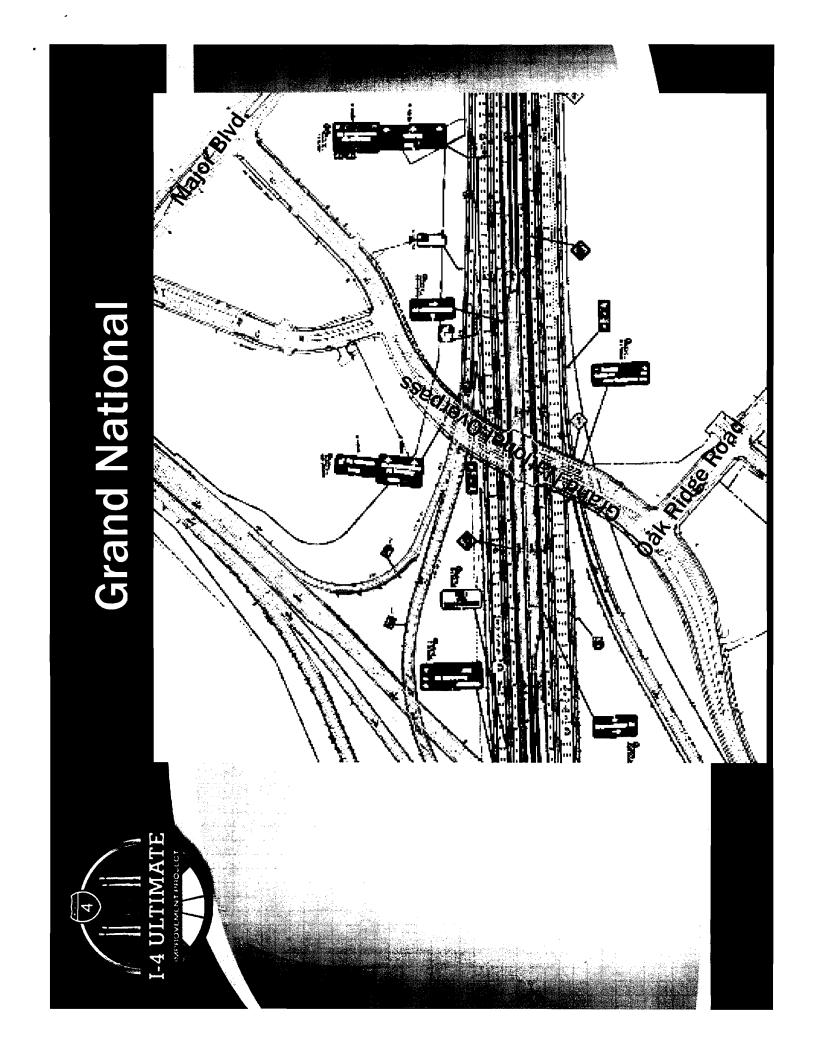





Questions?

Loreen Bobo, P.E.

FDOT I-4 Ultimate Program Manager

Loreen.Bobo@dot.state.fl.us

1.844.ULT.INFO (858.4636)

407.670.2341 (Office)

